

BULLETIN

Date:	10/25/2019	Number:	CT-01	Project #:	18157
Project Name:	West Ridge SF			Attached:	16/S6.1
Subject:	CHANGING RETAINING WALL SCHEDULE ON DETAIL 16/S6.1				
Drawings Affected:	Detail 16/S6.1				
Description/Action:					

This bulletin provides response to RFI, design clarifications and/or variation requests for the West Ridge Single Family Homes project located in Issaquah, Washington.



The cantilever retaining wall schedule without slab on grade as shown on detail 16 sheet S6.1 shall be replaced by the schedule attached along with this bulletin. The updated wall schedule has been calculated and verified by the engineer of record to be sufficient to carry the design loads. Detail 16/S6.1 has been updated with the new schedule and attached along with this bulletin.



10/25/2019


CALL WITH ANY QUESTIONS

Issued by:	Truc Thai	Date:	October 25, 2019
Distribution:			
Contact Information:			
Jeremy Pfarr	Milbrandt Architects		
Truc Thai	CT Engineering		

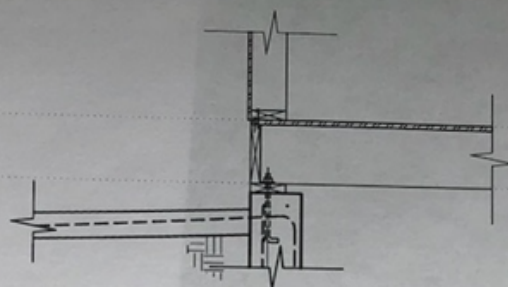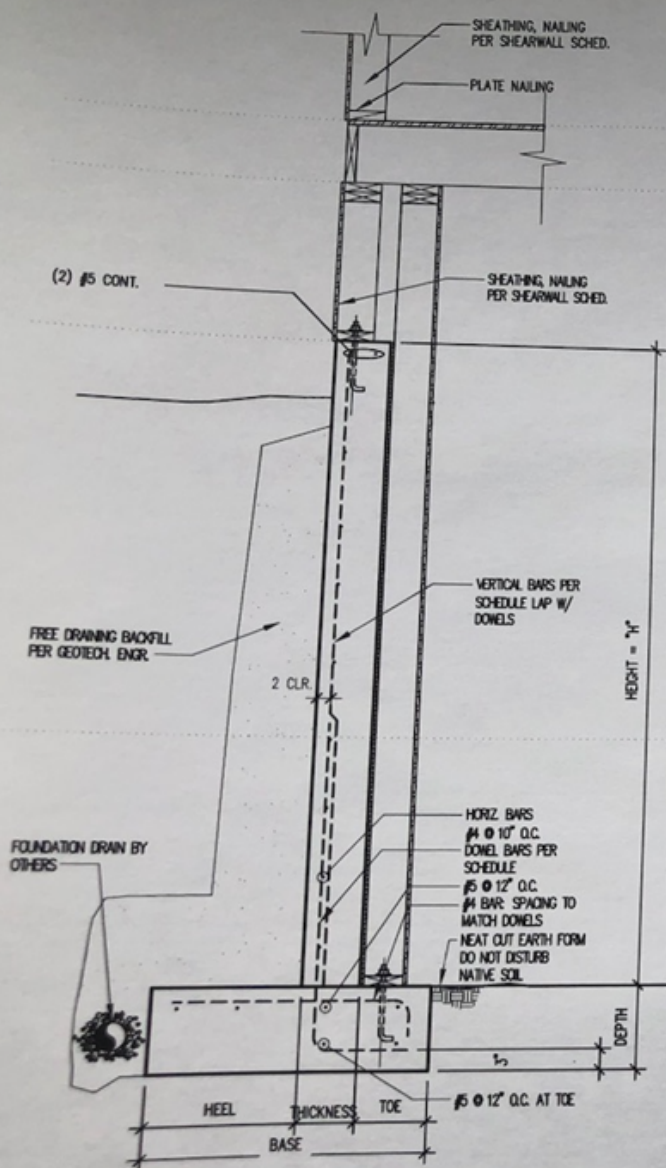


CANTILEVER RETAINING WALL SCHEDULE

WALL HEIGHT	HEEL	TOE	BASE	DEPTH	DOWELS	VERT. BARS	THICKNESS
0' TO 2'-0"	0'-4"	0'-4"	1'-4"	8"	#4 @ 18"	#4 @ 18"	8"
2'-1" TO 4'-0"	0'-6"	0'-6"	1'-8"	10"	#4 @ 18"	#4 @ 18"	8"
4'-1" TO 6'-0"	1'-10"	0'-8"	3'-0"	10"	#4 @ 12"	#4 @ 12"	8"
6'-1" TO 8'-0"	3'-2"	0'-8"	4'-4"	12"	#5 @ 10"	#5 @ 10"	8"
8'-1" TO 10'-0"	4'-7"	0'-8"	5'-8"	12"	#5 @ 8"	#5 @ 8"	8"
10'-1" TO 11'-0"	5'-2"	0'-8"	6'-4"	12"	#5 @ 6"	#5 @ 6"	8"
11'-1" TO 12'-0"	5'-10"	0'-8"	7'-0"	14"	#5 @ 5"	#5 @ 5"	8"

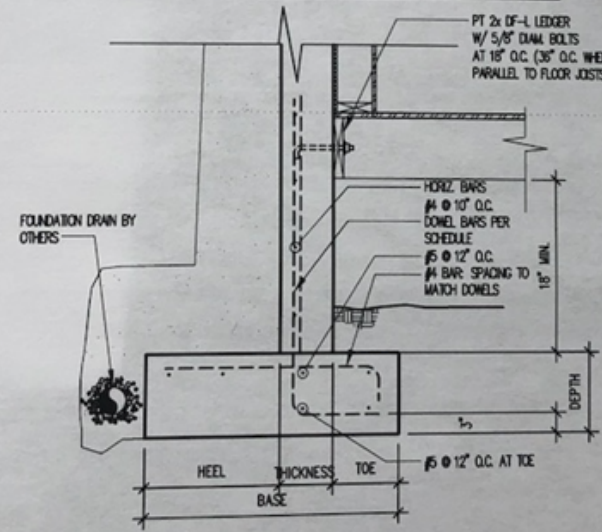

LEDGER OPTION

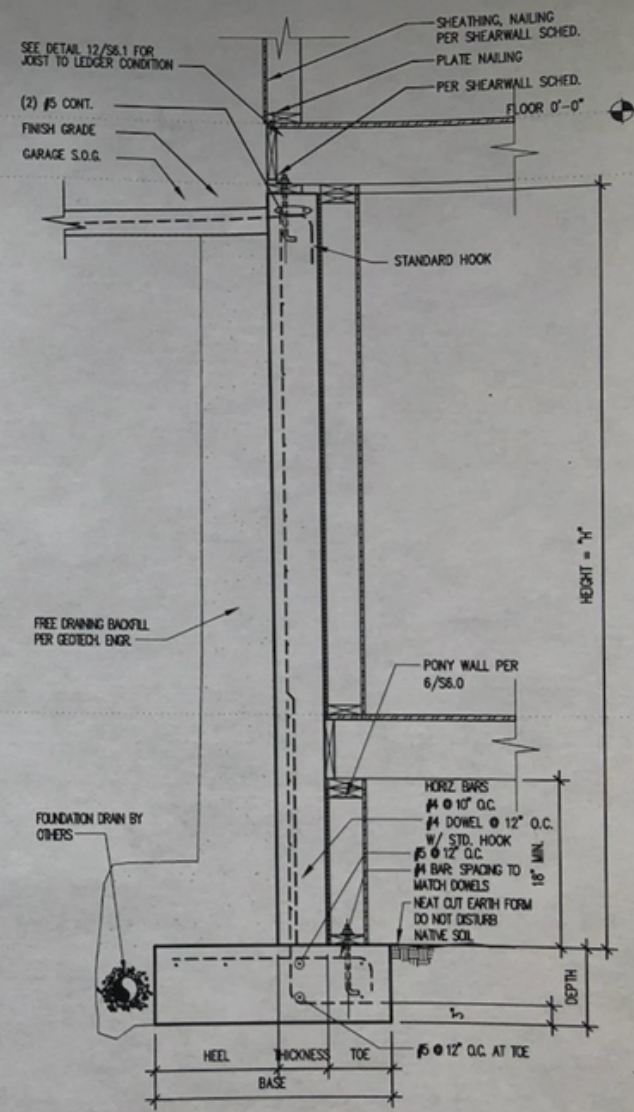

CANTILEVER RETAINING WALL (WITHOUT SLAB ON GRADE CONDITION)
