

REQUEST FOR INFORMATION

RFI# 0873

PROJECT: US Home Garage Corp Campus
BLDG 4: 730 Lake Drive
BLDG 5: 755 Lake Drive
Issaquah, WA 98027

RESPONSE REQUESTED BY: 11.02.2021

RESPONSE DATE:

OWNER: Costco Wholesale
999 Lake Drive
Issaquah, WA 98027

JOB NUMBER: 15-0035-03

CONTRACTOR: Ferguson Construction
13810 S.E. Eastgate Way, Suite 110
Bellevue, WA 98005-4417

ARCHITECT RECEIVED:

ARCHITECT: MG2 Corporation
1101 Second Avenue
Suite 100
Seattle, WA 98101-2923

SUBMITTED BY: Jay Clark

SUBJECT: P10 Trellis CC line G-F

REFERENCE: S/A

PROJECT TYPE: Building 5 - Parking Garage
w/ 1633 Parking Stalls

☒ ARCHITECT ☒ STRUCTURAL ☐ MECHANICAL ☐ ELECTRICAL ☐ CIVIL ☐ OTHER

CONTRACTOR REQUEST

Req. #	Comments
Request:	IT appears we missed a measurement for a trellis grid on CC/ G-F. We will replace the "C" on the perimeter to keep the fascia continuous, however, is there a possibility to have extension clips for the WF beam. Please advise.
Solution:	Extension Clips each end of WF

CONTRACTOR ATTACHMENTS

Name	Date	Type	Size	By
------	------	------	------	----

FORWARDED LOG


Date	Action	Discipline	Action By
------	--------	------------	-----------

Carry out the following instructions with no change in CONTRACT SUM or CONTRACT TIME. Submit an itemized proposal for the changes in CONTRACT SUM or CONTRACT TIME. This is not a direction to proceed.

ARCHITECT ATTACHMENTS

Name	Date	Type	Size	By
------	------	------	------	----

ENW
YES. ADD CLIP EXTENSIONS FOR WF BEAM. AT BOLTED CONNECTIONS FIT ALL AVAILABLE BOLTS (MID BEAM AND TOP AND BOT PLATES). ARCH TO VFY IF WE NEED TO ADD BOLTS FOR VISUAL CONSISTENCY. KEEP WELDS AT TOP AND BOT PLATES AS DETAILED.
CR
11-02-2021

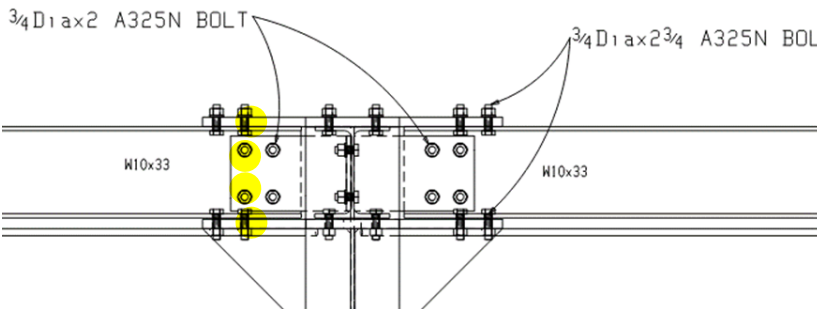


From: Ray Michlig
Sent: Monday, November 1, 2021 10:33 AM
To: Jay Clark
Cc: Greg Williams
Subject: Bad Dimension

Jay,

Can we get RFI approval in the works to Cesar? Ironworkers found a bay that was dimensioned wrong during as-builts. Must have measured between inner bolt pair. Occasionally had concrete blob on bolts, so remove duct tape from other pair for dimensioning. Apparently did not catch that one for center to center.

Want to see if we can weld these connections to the tabs provided, and piece in channel shortage as well.

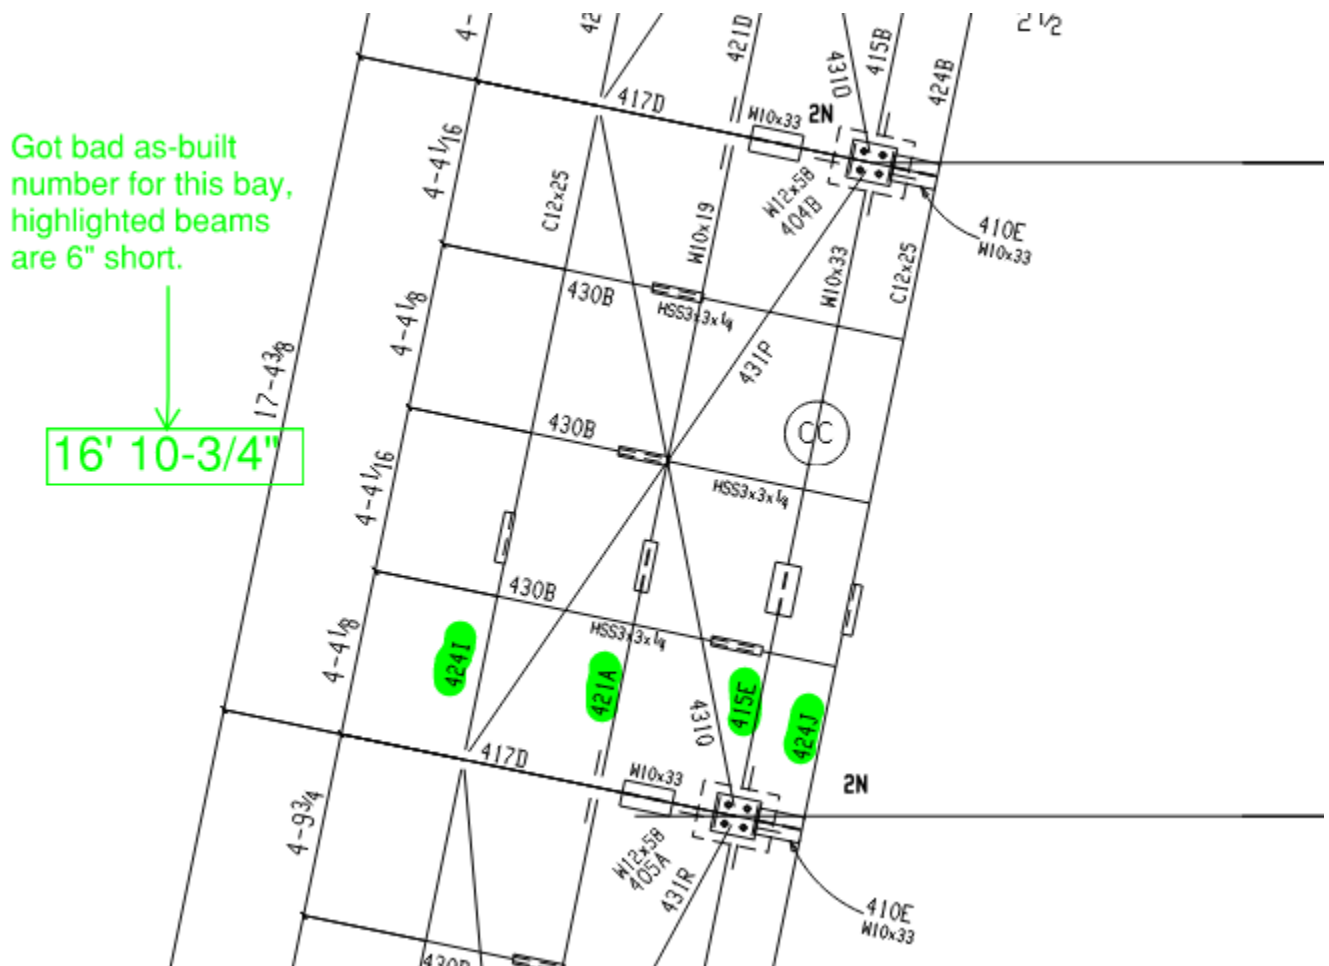

Ray Michlig

FERGUSON CONSTRUCTION, INC.

13810 SE EASTGATE WAY, SUITE 110 | BELLEVUE, WA 98005

T: 425-974-8400 | F: 425-974-8449 | C: 253-569-1605

raym@fergusonconstruction.com

www.fergusonconstruction.com

